

UW Bothell | Cascadia College STEM 4 Building Construction Bulletin



What is happening on the Bothell STEM4 Project:

December 2021

UWB-Cascadia College
STEM 4 Project
18330 110th Ave NE
Bothell, WA 98011



Primary Contact:

Mark Sweeters,
Construction Manager
sweeters@uw.edu
(206) 391 6207

Lease Crutcher Lewis Project Team:

Tony Kiehle, Superintendent
(206) 730 0242


Josh Van Kirk, Project Manager
(425) 681 8020

UW Project Delivery Group:

Harry Fuller, Project Manager
hfuller1@uw.edu
(206) 221 7448

This Community Bulletin is intended to serve as an update for upcoming work related to the Bothell STEM 4 project, as well as a means of notifying our campus community of any significant events that may impact the sidewalks and streets surrounding the project.

STEM4 foundation work has progressed over the last month. All the building's footings have now been completed. The crews have placed roughly 1,800 cubic yards of concrete thus far.

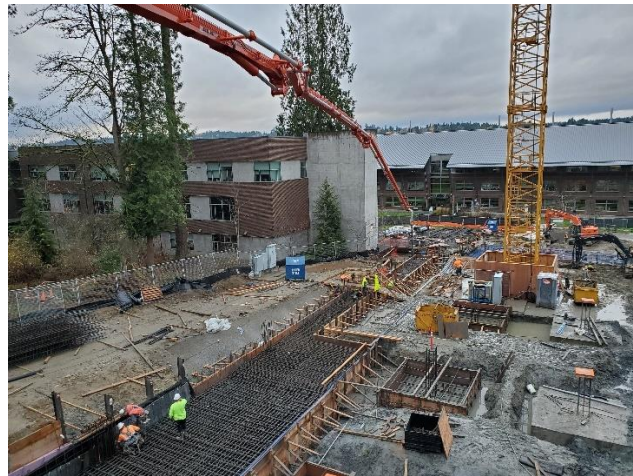

The tower crane has been erected to service the site during the construction of the building's structure.

With the completion of the footings, the project has kicked off the vertical concrete work starting with the Level 0 columns on the East half of the building. Slab on grade placement will begin at the end of the month with Level 0, then Level 1 in early January. Underground plumbing and electrical is currently being installed ahead of the slab on grade placements. Completion of the slab on grade paves the way for the mobilization of the horizontal formwork contractor beginning of the new year to start the elevated decks.

